



Huntington Beach Channel and Talbert Channel Repair Project

Huntington Beach Channel: South of Adams Ave. to east of Magnolia St. (approx. 3.1 miles) and;
Talbert Channel: South of Yorktown Ave. to west of Brookhurst St. (approx. 3 miles).

Current Stats




Construction is 30% complete

with an anticipated completion date of late 2023.



**6,800
LINEAR FEET**

6,800 linear feet (14M pounds!) of sheet piles have been installed.



40% complete!



Project Highlights

This project is vital to your community's safety and the protection of your home during major storm events. This project will:

- Maintain existing level of flood capacity
- Improve levees for seismic resiliency
- Meet levee recertification requirement


Are there any consequences of not completing project?

Yes, homeowners could be reintroduced into the floodplain and be required to pay mandatory flood insurance premiums.

Upcoming Activities

Curious about the next items on our punch list? The following items are our planned activities:

- Curbs and Gutters
- Maintenance Road
- Pavement Repairs
- Fiber-reinforced plastic caps
- Cable Railing

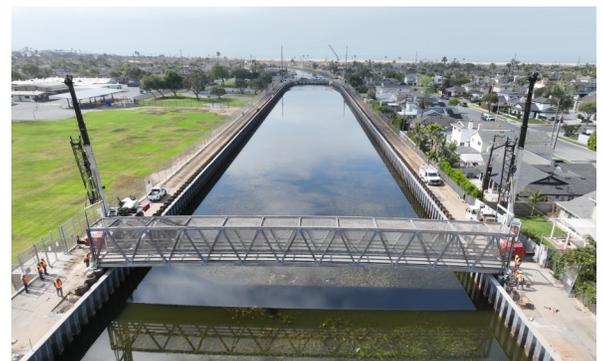

The bridge located at Eader Park in Huntington Beach will be opening in September 2022! We're looking forward to its completion and can't wait for you enjoy this upgrade to your community connections!

CONTACT INFORMATION



Teejay Areopagita



(714) 245-4500



ProjectInfo@ocpw.ocgov.com



ocpublicworks

VISIT US ONLINE @ ocpublicworks.com/HBT
